


Weislow - 630 Benicia Drive - Project Construction Schedule at 5-24-2013

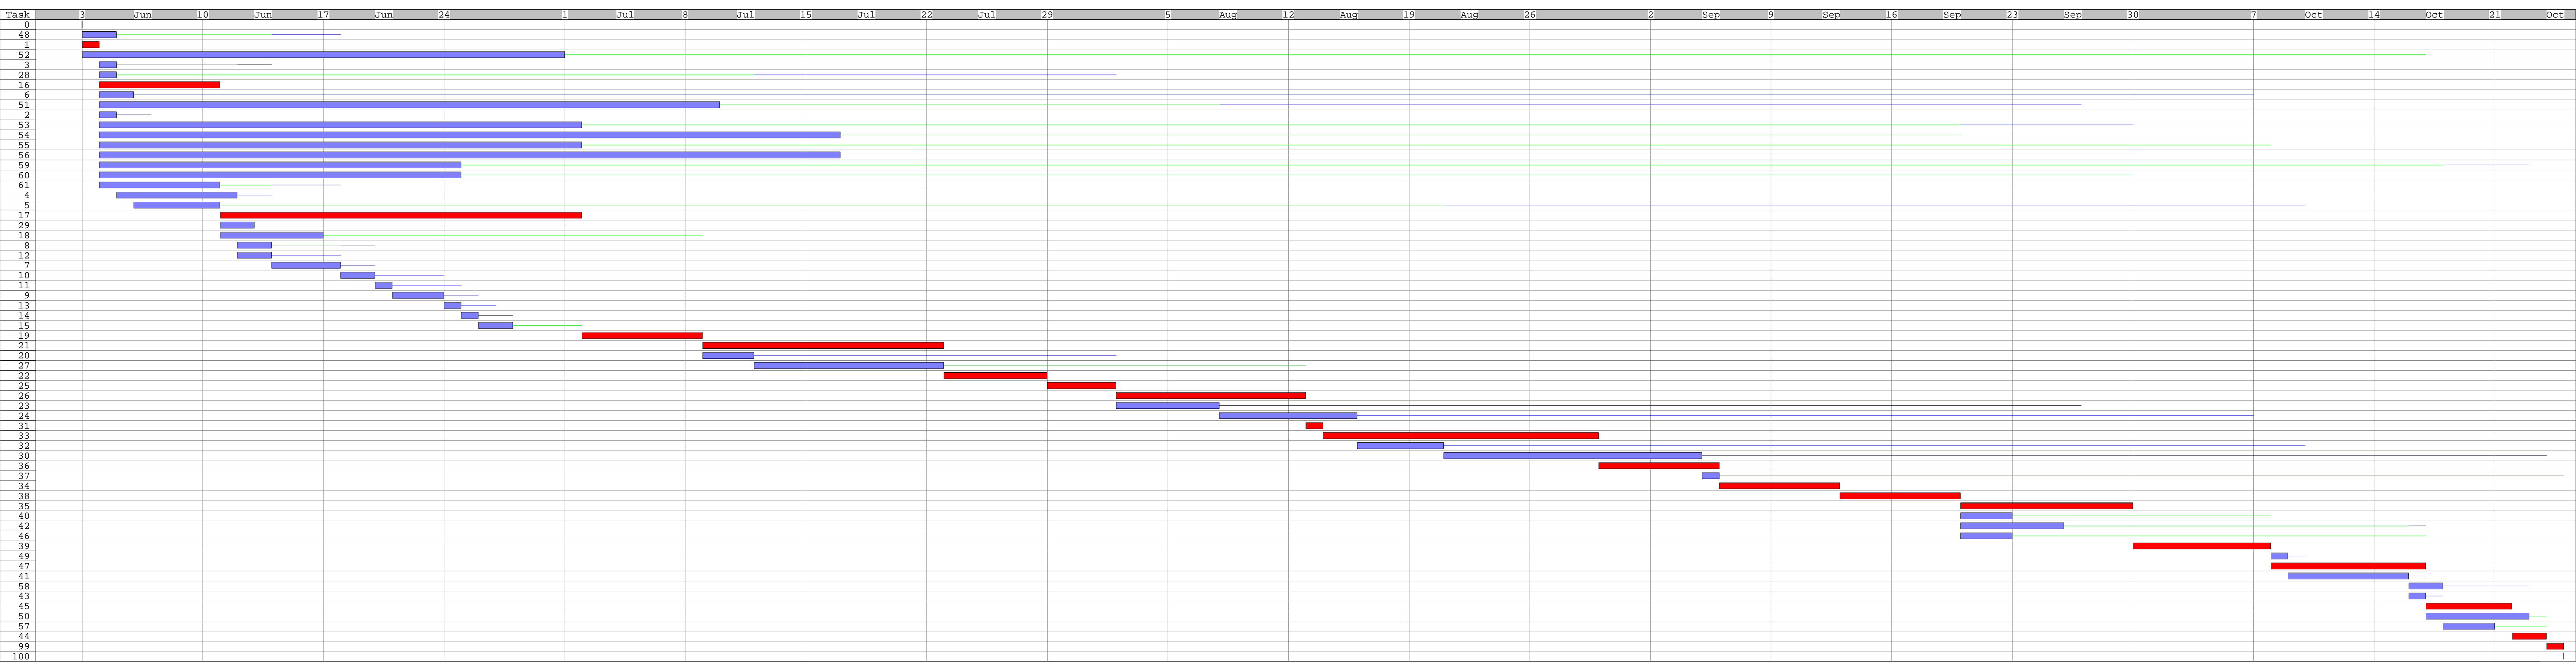

Activities List - for items listed at left of Diagram above

Num	Description	Start-Early-Finish	Start-Late-Finish	Slack	Free	Days	Delay	Cost	Labor	Units	Num	Description	Start-Early-Finish	Start-Late-Finish	Slack	Free	Days	Delay	Cost	Labor	Units	Num
0	Start Project	06-03-13 06-03-13	06-03-13 06-03-13	0	0	0	0	0	0	0	21	RIAttc/Insul	07-09-13 07-22-13	07-09-13 07-22-13	0	0	10	0	0	0	0	21
48	Move Irrig	06-03-13 06-04-13	06-14-13 06-17-13	9	7	2	0	0	0	0	48	20	BlidntWalls	07-09-13 07-11-13	07-30-13 08-01-13	15	0	3	0	0	0	20
1	MoveIn Layout	06-03-13 06-03-13	06-03-13 06-03-13	0	0	1	0	0	0	0	1	27	Fin RI ElMech	07-12-13 07-22-13	08-02-13 08-12-13	15	15	7	0	0	0	27
52	Order Applnc	06-03-13 06-28-13	09-19-13 10-16-13	76	76	20	0	0	0	0	52	22	Insp/ Rfhts	07-23-13 07-26-13	07-23-13 07-26-13	0	0	4	0	0	0	22
3	MvMainSwrWtr	06-04-13 06-04-13	06-13-13 06-13-13	7	5	1	0	0	0	0	3	25	PntEavExtChmn	07-29-13 08-01-13	07-29-13 08-01-13	0	0	4	0	0	0	25
28	StrtRIEMech	06-04-13 06-04-13	08-01-13 08-01-13	41	26	1	0	0	0	0	28	26	GuttrsRfg-TO	08-02-13 08-12-13	08-02-13 08-12-13	0	0	7	0	0	0	26
16	DemRfgFramg	06-04-13 06-10-13	06-04-13 06-10-13	0	0	5	0	0	0	0	16	23	DsWndwRefrme	08-02-13 08-07-13	09-23-13 09-26-13	35	0	4	0	0	0	23
6	CarpntChnges	06-04-13 06-05-13	10-03-13 10-04-13	85	0	2	0	0	0	0	6	24	WndrsSdgTrm	08-08-13 08-15-13	09-27-13 10-04-13	35	0	6	0	0	0	24
51	OrdWndDrsHdw	06-04-13 07-09-13	08-22-13 09-26-13	56	21	25	0	0	0	0	51	31	Insul FlrWalls	08-13-13 08-13-13	08-13-13 08-13-13	0	0	1	0	0	0	31
2	DemSwrWtr@Addtn	06-04-13 06-04-13	06-06-13 06-06-13	2	0	1	0	0	0	0	2	33	Drywll	08-14-13 08-29-13	08-14-13 08-29-13	0	0	12	0	0	0	33
53	OrdGtzShwPln	06-04-13 07-01-13	08-30-13 09-27-13	62	56	20	0	0	0	0	53	32	StoopsSpaSOG	08-16-13 08-20-13	10-07-13 10-09-13	35	0	3	0	0	0	32
54	OrdMeasCbnts	06-04-13 07-16-13	08-08-13 09-19-13	46	46	30	0	0	0	0	54	30	Paint Exter	08-21-13 09-04-13	10-10-13 10-23-13	35	0	10	0	0	0	30
55	OrdElcFxtTrm	06-04-13 07-01-13	09-10-13 10-07-13	68	68	20	0	0	0	0	55	36	Doors TrmHdw	08-30-13 09-05-13	08-30-13 09-05-13	0	0	4	0	0	0	36
56	OrdPlbFxtTrm	06-04-13 07-16-13	08-16-13 09-27-13	52	52	30	0	0	0	0	56	37	Spa Instal	09-05-13 09-05-13	10-24-13 10-24-13	35	35	1	0	0	0	37
59	OrdBthAcc'ry	06-04-13 06-24-13	10-02-13 10-22-13	84	81	15	0	0	0	0	59	34	Prime Inter	09-06-13 09-12-13	09-06-13 09-12-13	0	0	5	0	0	0	34
60	Order Tile	06-04-13 06-24-13	09-09-13 09-27-13	67	67	15	0	0	0	0	60	38	Paint Int#1	09-13-13 09-19-13	09-13-13 09-19-13	0	0	5	0	0	0	38
61	OrdBldMatls	06-04-13 06-10-13	06-11-13 06-17-13	5	3	5	0	0	0	0	61	35	CabntTrmInstall	09-20-13 09-27-13	09-20-13 09-27-13	0	0	6	0	0	0	35
4	Excav&doPnd	06-05-13 06-11-13	06-07-13 06-13-13	2	0	5	0	0	0	0	4	40	Shwr WlPlns	09-20-13 09-20-13	10-07-13 10-07-13	11	11	1	0	0	0	40
5	FinCarPort	06-06-13 06-10-13	10-07-13 10-09-13	85	56	3	0	0	0	0	5	42	Hwdw Floors	09-20-13 09-25-13	10-11-13 10-16-13	15	14	4	0	0	0	42
17	Order Truss	06-11-13 07-01-13	06-11-13 07-01-13	0	0	15	0	0	0	0	17	46	Vnnyl Flrgs	09-20-13 09-20-13	10-16-13 10-16-13	18	18	1	0	0	0	46
29	Blkg@ TopPlt	06-11-13 06-12-13	06-28-13 07-01-13	13	13	2	0	0	0	0	29	39	Ctops Splash	09-30-13 10-07-13	09-30-13 10-07-13	0	0	6	0	0	0	39
18	DemAtcItems	06-11-13 06-14-13	07-02-13 07-08-13	15	15	4	0	0	0	0	18	49	Plbg Sinks	10-08-13 10-08-13	10-09-13 10-09-13	1	0	1	0	0	0	49
8	PrpFndBaltg	06-12-13 06-13-13	06-18-13 06-19-13	4	2	2	0	0	0	0	8	47	ElMechTrim	10-08-13 10-16-13	10-08-13 10-16-13	0	0	7	0	0	0	47
12	InspPrStrpFnd	06-12-13 06-13-13	06-14-13 06-17-13	2	0	2	0	0	0	0	12	41	Tile Floors	10-09-13 10-15-13	10-10-13 10-16-13	1	0	5	0	0	0	41
7	Frame Flr Addtn	06-14-13 06-17-13	06-18-13 06-19-13	2	0	2	0	0	0	0	7	58	Plbg FxtTrm	10-16-13 10-17-13	10-21-13 10-22-13	3	0	2	0	0	0	58
10	Rls u/NewFlr	06-18-13 06-19-13	06-20-13 06-21-13	2	0	2	0	0	0	0	10	43	Basebd	10-16-13 10-16-13	10-17-13 10-17-13	1	0	1	0	0	0	43
11	Insly/NewFlr	06-20-13 06-20-13	06-24-13 06-24-13	2	1	0	0	0	0	0	11	45	Appli ances	10-17-13 10-21-13	10-17-13 10-21-13	0	0	3	0	0	0	45
9	Insp u/Flr	06-21-13 06-21-13	06-25-13 06-25-13	2	0	1	0	0	0	0	9	50	Paint Int#2	10-17-13 10-22-13	10-18-13 10-23-13	1	1	4	0	0	0	50
13	Close Floor	06-24-13 06-24-13	06-26-13 06-26-13	2	0	1	0	0	0	0	13	57	InstBathAcc	10-18-13 10-18-13	10-23-13 10-23-13	3	3	1	0	0	0	57
14	Demo SdgW	06-25-13 06-25-13	06-27-13 06-27-13	2	0	1	0	0	0	0	14	44	Carpet	10-22-13 10-23-13	10-22-13 10-23-13	0	0	2	0	0	0	44
15	Frame Wlls	06-26-13 06-27-13	06-28-13 07-01-13	2	2	2	0	0	0	0	15	99	Final Cleang	10-24-13 10-24-13	10-24-13 10-24-13	0	0	1	0	0	0	99
19	Frame Roof	07-02-13 07-08-13	07-02-13 07-08-13	0	0	4	0	0	0	0	19	100	End of Project	10-24-13 10-24-13	10-24-13 10-24-13	0	0	0	0	0	0	100
